

**Walker's Court,
London, W1**

Blenheim House
construction

Monthly Works Forecast

17/01/2017

Contact details in case of query:

Mike Jones

Project Manager

Mobile: 07775715287

mjones@bhcltd.co.uk

Paul Donohoe

Senior Site Manager:

Mobile: 07920 533686

pdonohoe@bhcltd.co.uk

**Westminster City Council
(Highways)**

Dean Bermingham

Highways Licensing Officer

Public Protection and Licensing

Westminster City Council

4th Floor West

Westminster City Hall

64 Victoria Street

London SW1E 6QP

Tel: 0207 641 3802

Fax: 0207 641 3159

dbermingham@westminster.gov.uk

General Enquires

Jessica Stewart

Comm Comm UK

020 7125 0421

jessicas@commcommuk.com

Walker's Court – January Forecast

Dear Neighbour


The following outlines works that we will be conducting in the coming month:

- UKPN will be completing the installation of ductworks and cables to the new sub-station in Walker's Court from the road to Brewer Street this week
- Tuesday 17 January to Friday 27 January - The conveyor will be re-erected at the Brewer Street end of Walker's Court and encased in timber hoarding
- Monday 23 January - The scaffolding, which is currently at the Peter Street end of Walker's Court will be extended through Walker's Court down to Brewer Street. The works will take appropriately three weeks to complete and will be carried out from 6am to 12pm.

Brewer Street Scaffolding - Monday 23 January

- Works will commence on Monday 23 January 2017 to scaffold the 4-6 Brewer Street elevations. The footpath on the side of 4-6 Brewer Street will be closed at all times until the scaffolding is struck. A scaffolding lorry will be parked on Brewer Street throughout the duration of the works from 7.30am to 4.30pm
- Monoflex sheeting will be used to screen off where the scaffold is built next to 2 Brewer Street. Security, in the form of a laser beam and camera, will be installed at first floor and will be activated when Blenheim House Construction is off-site
- The Madam JoJo's artwork on Brewer Street will be moved onto the front of the scaffold hoardings
- Please see map overleaf for more details.



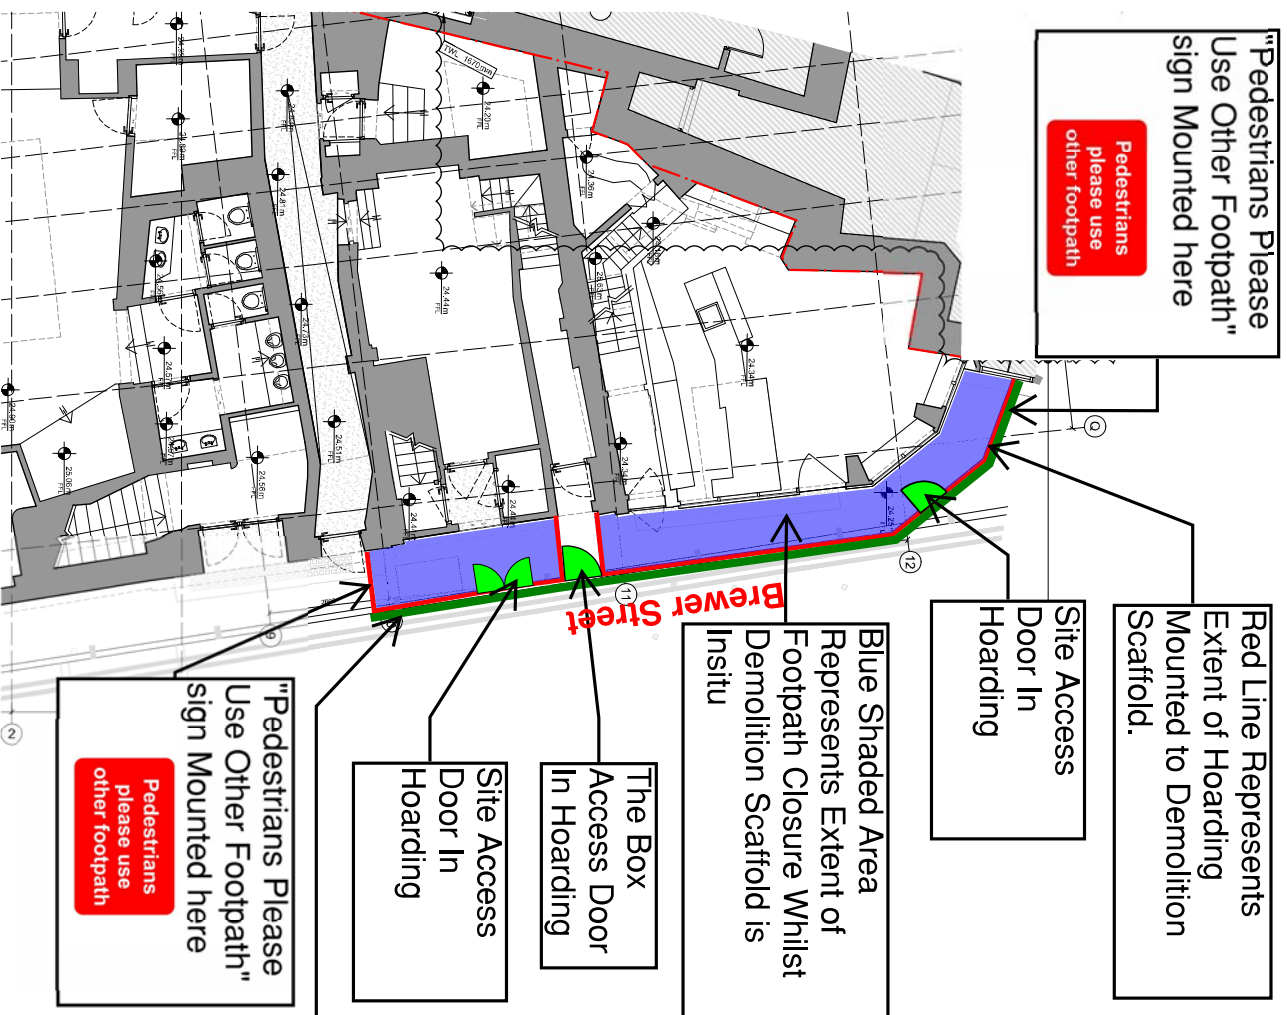

General Notes

Scaffold to be erected during normal working hours

Hoardings to be erected during normal working hours.

Hoardings and Bulks Timbers to be Illuminated with Bulkhead fittings

Illuminated Bulk Timbers on Edge of Hoarding

BREWER STREET DEMOLITION SCAFFOLD ARRANGEMENT.

BLENHHEIM HOUSE CONSTRUCTION., WALKERS COURT, SOHO
