

Weekly Works Forecast

W/C 5/9/16

Contact details in case of query:

Steve McIntyre

Senior Project Manager
Mobile: 07423 434419
smcintyre@bhcltd.co.uk

Paul Donohoe

Senior Site Manager:
Mobile: 07920 533686
pdonohoe@bhcltd.co.uk

Westminster City Council (Highways)

Dean Bermingham
Highways Licensing Officer
Public Protection and Licensing
Westminster City Council
4th Floor West
Westminster City Hall
64 Victoria Street
London SW1E 6QP
Tel: 0207 641 3802
Fax: 0207 641 3159
dbermingham@westminster.gov.uk

General Enquires

Jessica Stewart
Comm Comm UK
020 7125 0421
jessicas@commcommuk.com

Walkers Court, Works Forecast – W/C 5/9/16

Dear Neighbour,

The following outlines works that we will be conducting in the coming week;

- Strip Out of 4&6 Brewer Street buildings
- Strip Out of 6 Walkers Court demise
- Construction of capping beam in Walkers Court (see attached diagram)
- Brickwork to new build structure within Walkers Court demise
- Installation of conveyor system


Advance Warning

Construction of capping beam in Walkers Court w/c 1/8/16 – two way pedestrian traffic will be possible up and down walkers court but some sections will be narrowed to 1500mm during the construction works. Signage regarding local businesses and Berwick Street market will be in place to inform the public that all businesses are open. These works are currently in delay by approximately 7 days due to unforeseen ground conditions, we apologise for any inconvenience caused during these works.



Registered site
www.ccscheme.org.uk

HOARDING PHASES & DATES

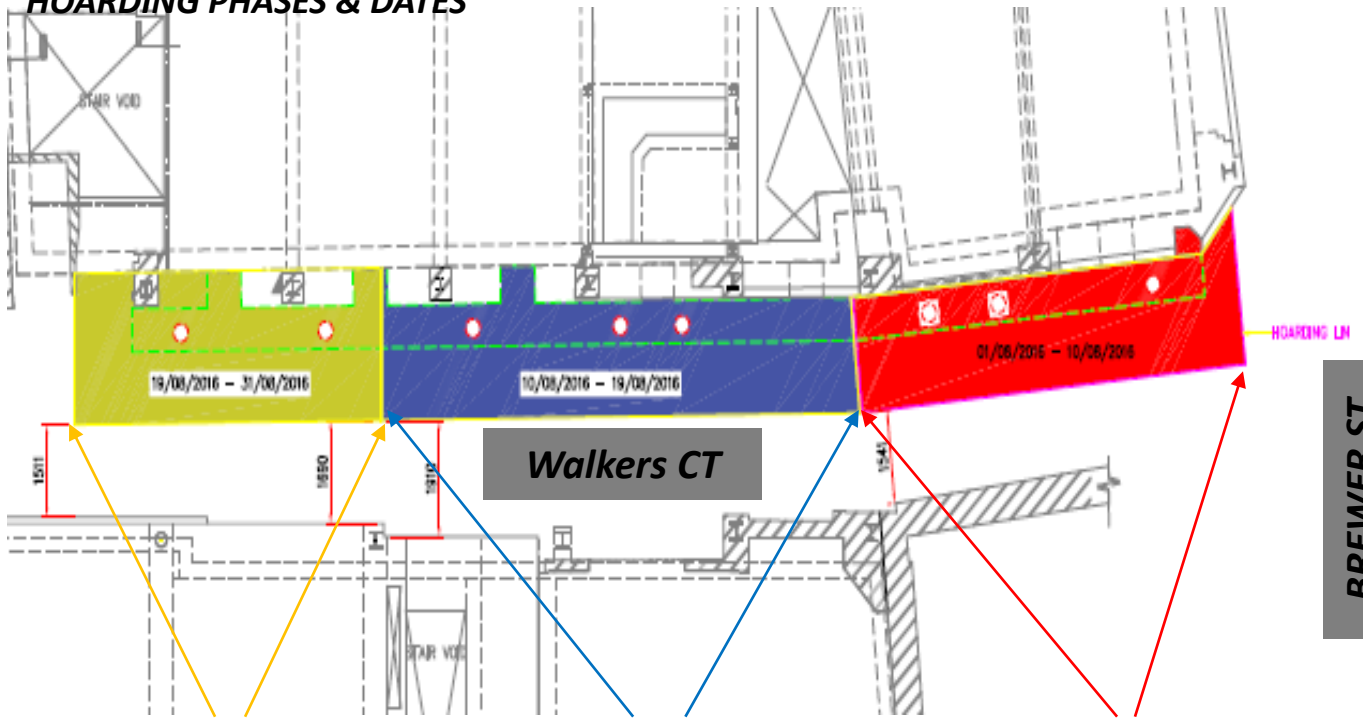

YELLOW = 31/8/16 to 9/9/16 BLUE = 19/8/16 to 31/8/16 RED = 1/8/16 to 19/8/16



Minimum pavement width during each phase of works will be 1500mm.

Two-way pedestrian movement will be possible at all times during the works.

Signage regarding local businesses and the market being open as usual will be posted at the entrance to Walkers Court and marshals will be on hand to direct pedestrians
